



EARTHINVLAB


MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

HOLE No: TP 01

Sheet 1 of 1

JOB NUMBER: EIL\_324.4

Scale  
1:15

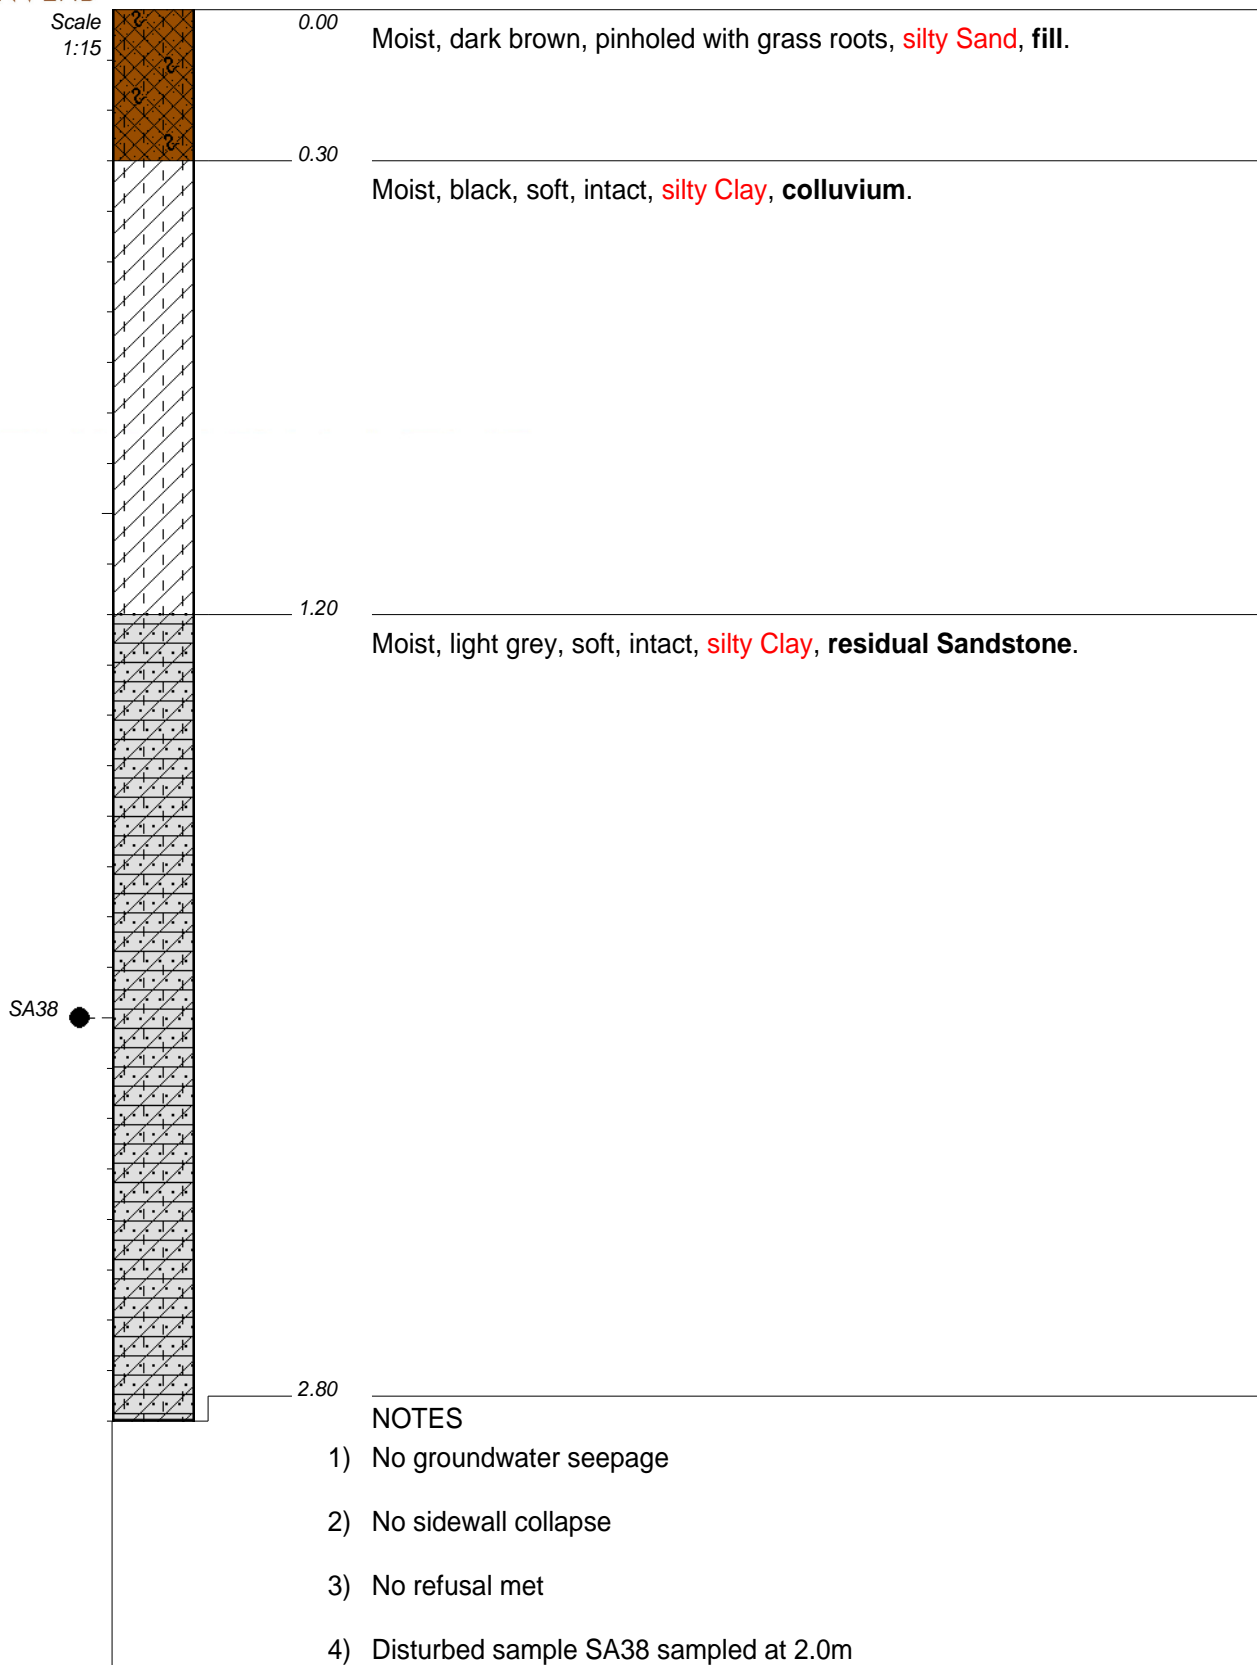

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFIED BY : Lukhanyo Gqobo  
TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION : 0.0km WP 4  
DIAM : 0.8 x 2.0 x 3.0 m  
DATE :  
DATE : 03 November 2023  
DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION : 245m  
X-COORD : 30°55'11.20"E  
Y-COORD : 29°49'3.90"S

HOLE No: TP 01




EARTHINVLAB

MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

HOLE No: Tp 02  
Sheet 1 of 1

JOB NUMBER: EIL\_324.4

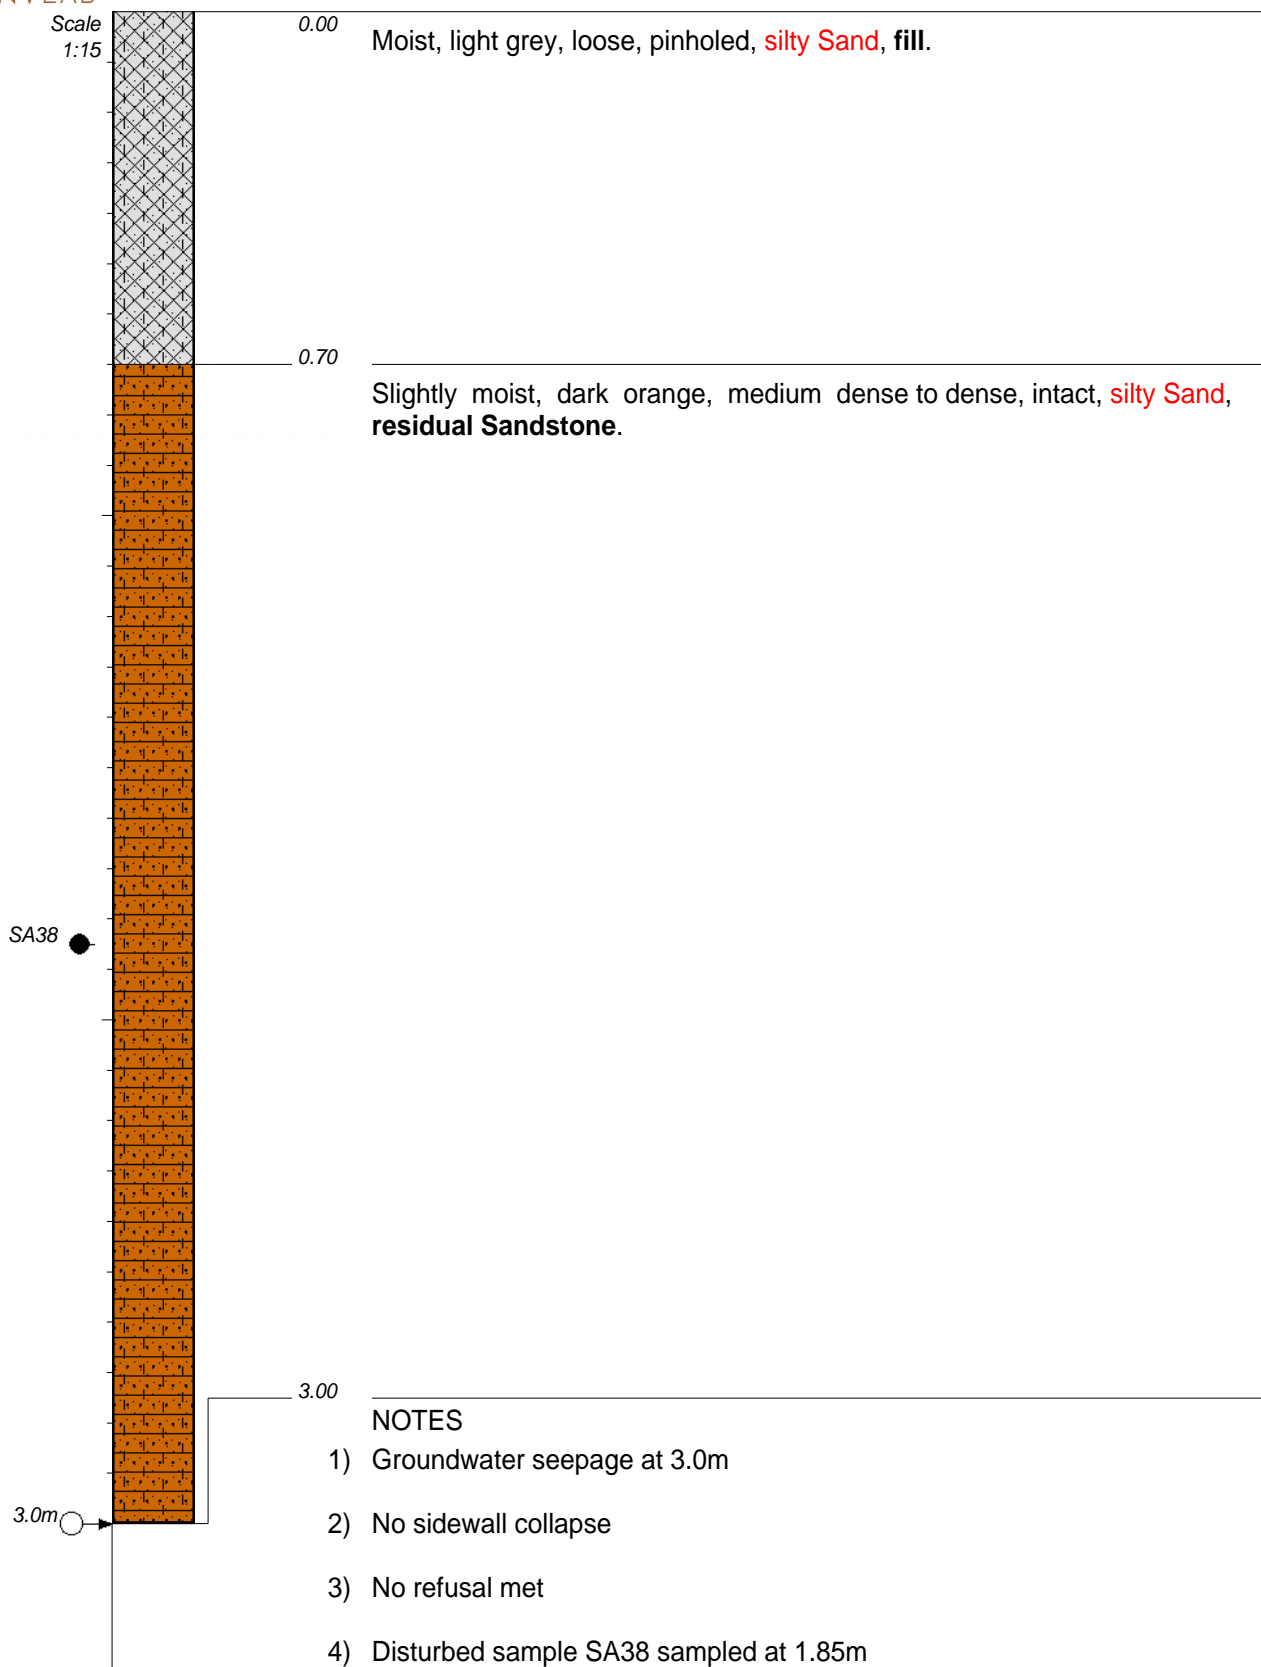

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFIED BY : Lukhanyo Gqobo  
TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION : 0.35km WP 4  
DIAM : 0.8 x 2.0 x 3.0 m  
DATE :  
DATE : 03 November 2023  
DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION : 241m  
X-COORD : 30°55'15.17"E  
Y-COORD : 29°49'15.01"S

HOLE No: Tp 02




EARTHINVLAB

MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

HOLE No: Tp 04  
Sheet 1 of 1

JOB NUMBER: EIL\_324.4

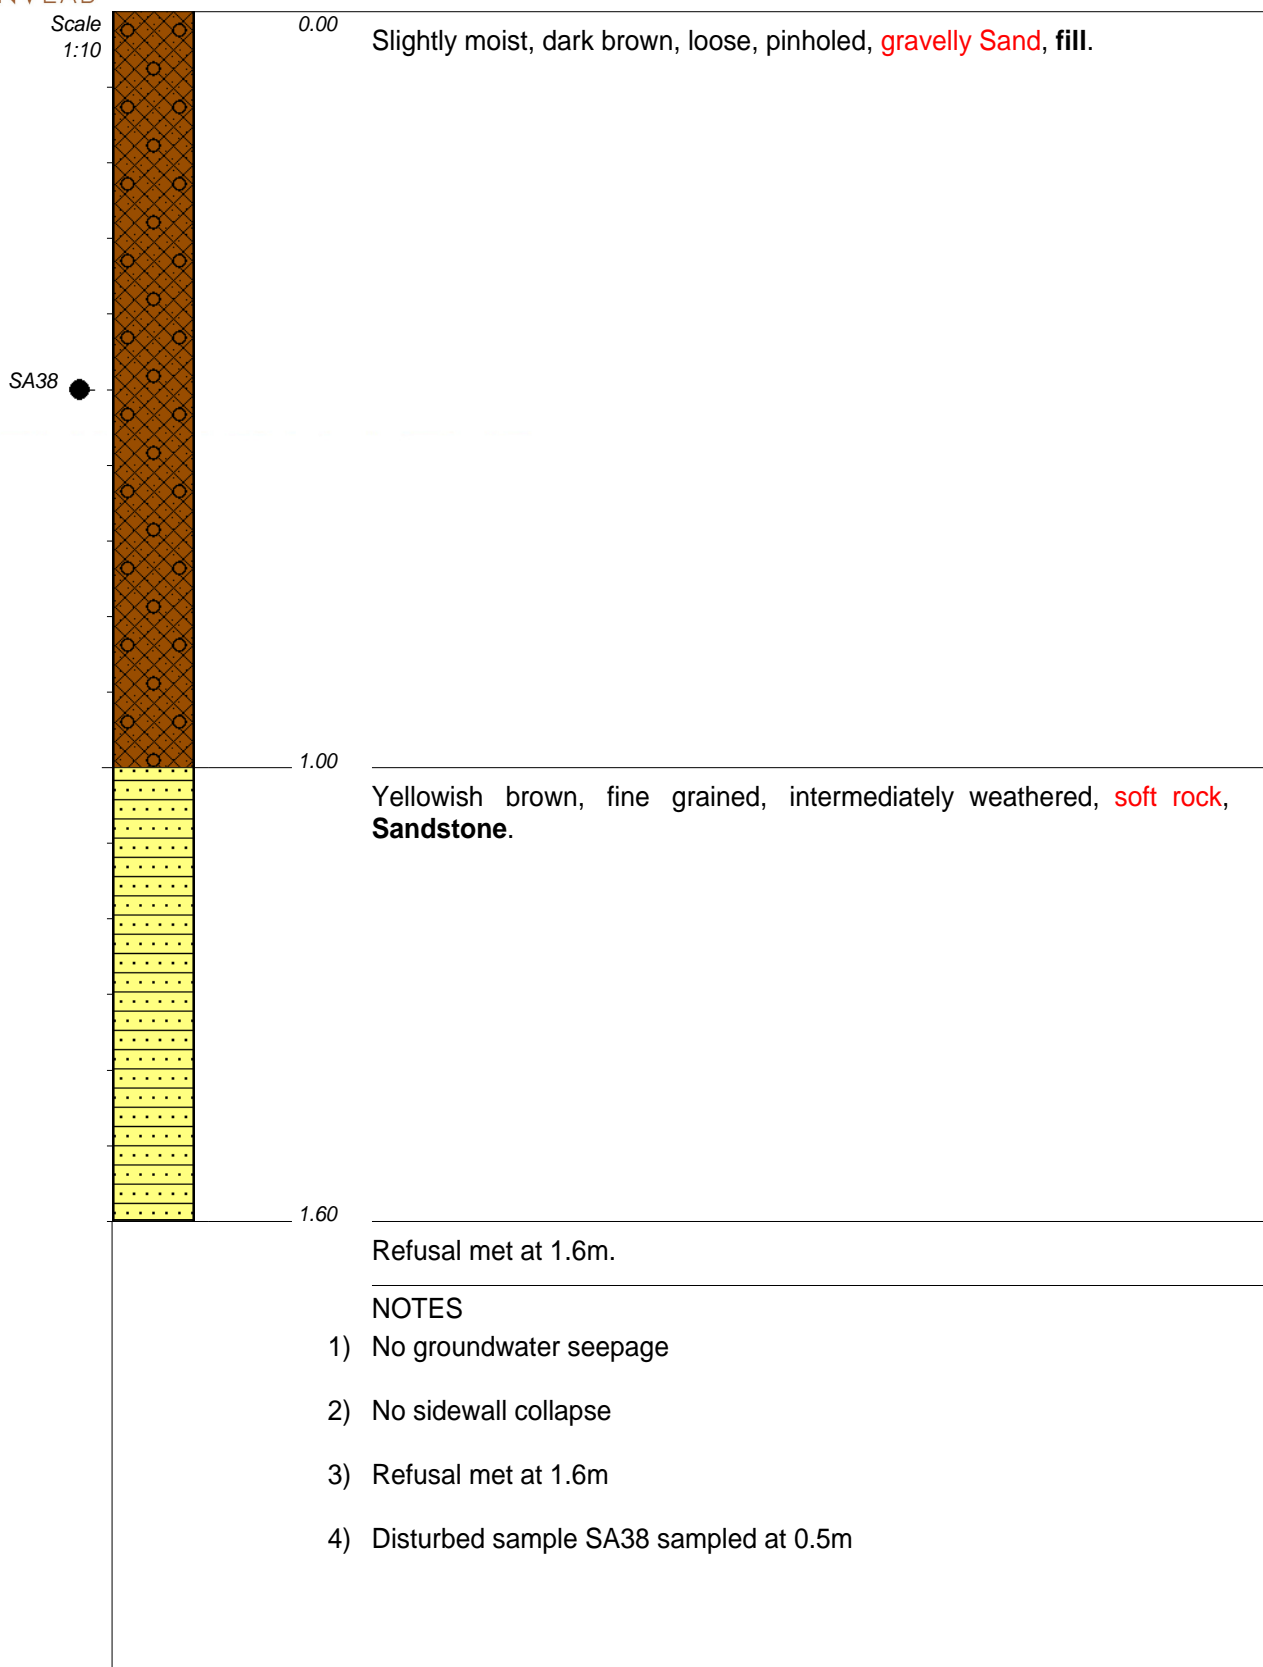

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFIED BY : Lukhanyo Gqobo  
TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION : 1.0km WP 4  
DIAM : 0.8 x 2.0 x 3.0 m  
DATE :  
DATE : 03 November 2023  
DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION : 239m  
X-COORD : 30°55'2.92"E  
Y-COORD : 29°49'24.01"S

HOLE No: Tp 04



EARTHINVLAB

MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

HOLE No: Tp 05  
Sheet 1 of 1

JOB NUMBER: EIL\_324.4

Scale  
1:10

0.00

Slightly moist, dark brown, loose to medium dense, pinholed, **silty Sand, colluvium.**

0.60

Slightly moist, reddish brown blotched yellow, dense, intact, **silty Sand, residual Sandstone.**

SA38

1.90

Refusal met at 1.9m.

#### NOTES

- 1) Np groundwater seepage encountered
- 2) No sidewall collapse
- 3) Refusal met at 1.9m
- 4) Disturbed sample SA38 sampled at 1.25m

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFIED BY : Lukhanyo Gqobo  
TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION : 1.25km WP 4  
DIAM : 0.8 x 2.0 x 3.0 m  
DATE :  
DATE : 03 November 2023  
DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION : 240m  
X-COORD : 30°54'52.47"E  
Y-COORD : 29°49'21.56"S

HOLE No: Tp 05



EARTHINVLAB

MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

HOLE No: Tp 06

Sheet 1 of 1

JOB NUMBER: EIL\_324.4

Scale  
1:10

0.00

Slightly moist, dark brown, loose to medium dense, pinholed, **silty Sand**,  
**colluvium**.

0.35

Moist, purple, dense, intact, **silty Sand**, **residual Sandstone**.

SA38

1.65

Refusal met at 1.65m

#### NOTES

- 1) No groundwater seepage
- 2) No sidewall collapse
- 3) Refusal met at 1.65m
- 4) Disturbed sample SA38 sampled at 1.0m

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFIED BY : Lukhanyo Gqobo  
TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION : 1.55km WP 4  
DIAM : 0.8 x 2.0 x 3.0 m  
DATE :  
DATE : 03 November 2023  
DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION : 246m  
X-COORD : 30°54'44.67"E  
Y-COORD : 29°49'25.58"S

HOLE No: Tp 06



EARTHINVLAB

MMK Group  
Southern Aquaduct Work Package 4 High Wycombe Road  
to Roger Shishi Road

**LEGEND**  
Sheet 1 of 1

JOB NUMBER: EIL\_324.4

	GRAVELLY	{SA03}
	SAND	{SA04}
	SILTY	{SA07}
	CLAY	{SA08}
	SANDSTONE	{SA11}
	FILL	{SA32}
	DISTURBED SAMPLE	{SA38}
	ROOTS	{SA40}
	WATER SEEPAGE/water strike	{CH50}

CONTRACTOR :  
MACHINE :  
DRILLED BY :  
PROFILED BY :

TYPE SET BY : Lukhanyo Gqobo  
SETUP FILE : STANDARD.SET

INCLINATION :  
DIAM :  
DATE :  
DATE :

DATE : 18/03/2024 15:02  
TEXT : ..eRDtoRogerShishiRoad.txt

ELEVATION :  
X-COORD :  
Y-COORD :

**LEGEND**  
SUMMARY OF SYMBOLS
